

DOCUMENT 96 · STARTING POINTS AND IMPLEMENTATION JOURNEY

Starting points and implementation journey

Where each company starts according to the AI and governance it already has, what it does at each stage, who does it and with what evidence, without lowering what the framework requires in the end

Fernando García Varela Version 0.2 28-09-2026

Thresholds and priorities validated (28-09-2026)

6	5	22	5
typical starting points	modifiers	journey milestones	stages up to the declaration of application

IN THIS DOCUMENT

01 Purpose and scope

02 Starting points

03 The five stages

04 The journey milestones

05 What falls to each role

06 Three example journeys

07 Relationship with other documents

08 Associated tools and templates

09 Related documents

10 Version control

Legal notice and disclaimer. SEVEN-G is a reference methodological framework provided "as is" and for information purposes only. It does not constitute legal, regulatory, financial or professional advice, nor does it guarantee compliance with any law or standard. References to general regulation (such as the EU AI Act, the GDPR, DORA or NIS2), to technical standards and to regulation specific to each sector or jurisdiction may be incomplete, may not apply to a particular case or may become out of date as a result of regulatory changes, interpretations or supervisory positions after their consultation date. **Each organisation that uses SEVEN-G is solely responsible for identifying the regulation that applies to it, verifying that it is current and certifying its own regulatory compliance,** with the appropriate qualified advice. This methodology is a generic, free aid shared with the community so that nobody has to start from scratch; each person or organisation can and should adapt it to its own use. It must not be inferred that its legally sensitive parts have been reviewed by legal counsel: those reviews, for each company or sector, are the ultimate responsibility of the company, consultant or organisation that uses it. Although every effort is made to keep it up to date, some regulation may have changed without being reflected here. To the fullest extent permitted by law, the author accepts no responsibility whatsoever for the effects of its application in any organisation or for its full applicability. The methodology does not grant certification of any kind. The author accepts no liability for any use made of this content or for any decisions taken on the basis of it. The data, figures, companies and cases in the examples are fictitious or illustrative.

THE ESSENTIALS

Recommended

Used to choose the order of implementation according to the company's starting point (no AI, third-party AI, automation, ML, many pilots or at scale). Rule that is never skipped: the starting point changes the order, the emphasis and the timetable, never what is required in the end; the seven conditions of the declaration of application (01 §14) are the same for everyone. Tool T23 runs the questionnaire and produces the plan.

Obligation matrix and layered reading (document 94)

01

Purpose and scope

The implementation guide (document 90) describes **what** must be in place and within what maximum time limit: Lite or Enterprise scope, prerequisites, 90-day plan, regularisation of what already exists and roadmap up to the declaration of application. But companies do not start from the same place.

One with no AI in production and another with forty predictive models and two agents that act need **to start with different things**, even though they must reach the same destination.

This document answers three questions:

1. **Where is the company starting from?** Six typical starting points (archetypes), five modifiers and a twelve-question questionnaire to assign them (section 2).
2. **What does it do first, what next, and who does it?** Five stages and twenty-two milestones, each with its evidence, the question from document 11 that substantiates it and its priority according to the starting point (sections 3 and 4), plus what falls to each role (section 5).
3. **What does it look like in practice?** Three fictitious journeys (section 6).

Tool **T23 · Implementation journey** applies this document: it runs the questionnaire, assigns the starting point and shows the journey prioritised by stage and by role.

Why it matters. If a company with no AI starts by setting up every body, it ends up in bureaucracy without use cases. If a company with agents in production starts with the use case record, it leaves uncontrolled what is already acting on customers or money. The starting point decides **what is done first**, not what is required in the end.

What this document does not do. It creates no rules: phases, gates, roles, time limits and conditions are in documents 01, 20, 21, 30 and 90, and the obligation level of each piece in 94. If this document diverges from them, they prevail. Nor does it replace the maturity diagnosis (document 11): it uses it.

Starting points

2.1 The six archetypes

Code	Archetype	How it is recognised	Typical risk	Where it starts	What can wait
PP-A	Ground zero	No own AI in production and none knowingly contracted. There is usually unauthorised use of generative assistants.	Unauthorised use with company data; ideas without an owner.	Mandate and sponsor; inventory of unauthorised use; acceptable use policy and basic literacy; use case record (P01) and T01 register for the first ideas.	Regularisation (there is nothing to regularise); agent security and operation, until a case reaches phase 4.
PP-B	Third-party AI user	Assistants in the office suite, SaaS with AI included or contracted AI; it does not develop.	AI that comes in without passing through any gate (54 §5); licence costs without measured adoption.	Inventory of the AI included in what is contracted (36 §8, P55); requirements on suppliers N1–N3 (36, P14); acceptable use policy; measuring the assistant as a cross-unit initiative with a ladder by unit (40 §7.2).	In-house building (53) and part of the technical cycle, until it builds something.
PP-C	Automator	Rule-based automation or RPA in production, with a centre of excellence or automation team; little or no AI that learns.	Confusing automation with AI; moving from bots to agents (A2/A3) without the controls of document 35.	Turning the centre of excellence into the seed of the AI Office (30); an inventory that separates what is AI from what is not (32); a portfolio of cases that replace rules with AI, each with its record.	Its process discipline is an asset: redesigning the process end to end (IT-P2) comes more easily to it.
PP-D	In-house AI in production	Own models in production — predictive (ML, vision, optimisation) or generative AI integrated into processes—, without agents that act or both at once. There is usually a data team and, sometimes, model validation.	Models in production without a continuity review; a new type of AI coming in outside the existing governance.	Regularisation of what is in production (90 §5, review equivalent to G7); bringing existing model validation into G5 and R6; drift and monitoring (52); inventory with regulatory classification.	What belongs to the type of AI it does not have yet: with ML only, knowledge sources (51; D3.08), evaluation with test sets (D4.08) and bias in responses (52 §4.2.7); with generative AI only, data drift and validation of predictive models (52).

Code	Archetype	How it is recognised	Typical risk	Where it starts	What can wait
PP-E	Many pilots	Several generative AI proofs of concept (as a guide, three or more) and none or one in production.	"Pilot purgatory": cost without value and without a decision to stop.	Registering every pilot in T01 in its real phase; G3 as the stop gate and the funnel to stop or scale; value hypothesis and baseline (40, P08, P09) before more budget.	The full structure of bodies: first the decision on the portfolio, then the rest.
PP-F	At scale	Agents that act (A2 or A3) in production, or predictive ML and generative AI integrated into processes at the same time.	Regulatory and security exposure that is already real; governance lagging behind use.	Segregated roles and AI Auditor immediately; complete inventory with classification; agent security (35) and suppliers (36); regularisation prioritised by risk; board dashboard and transformation index.	Nothing: everything is mandatory and urgent.

Why it matters. Naming the starting point avoids two opposite mistakes: copying the plan of another company that started from somewhere else, and believing that, because something already exists (a data committee, an automation centre), there is no need to adapt it.

2.2 Assignment rule


It is applied in this order and the **first archetype** whose conditions are met is assigned. Later archetypes whose positive condition is also met (without their exclusions: for example, "rules or RPA in production" is enough for the PP-C trait even if there is also ML) are added as **traits**: their priority milestones are added to the journey (section 4.3, rule 5).

Order	Archetype	Condition
1	PP-F	A2 or A3 agents in production, or predictive ML and generative AI integrated into processes at the same time.
2	PP-E	Three or more AI pilots under way, mostly generative AI, and at most one generative AI system in production.
3	PP-D	In-house AI in production: predictive ML, vision or optimisation with learning, or generative AI integrated into processes.

Order	Archetype	Condition
4	PP-C	Rules or RPA in production, with no AI that learns in production.
5	PP-B	Third-party AI included in products or corporate assistants, with no in-house build in production.
6	PP-A	None of the above.

How the starting point is assigned

The first archetype that is met is assigned; the following ones that are also met are traits

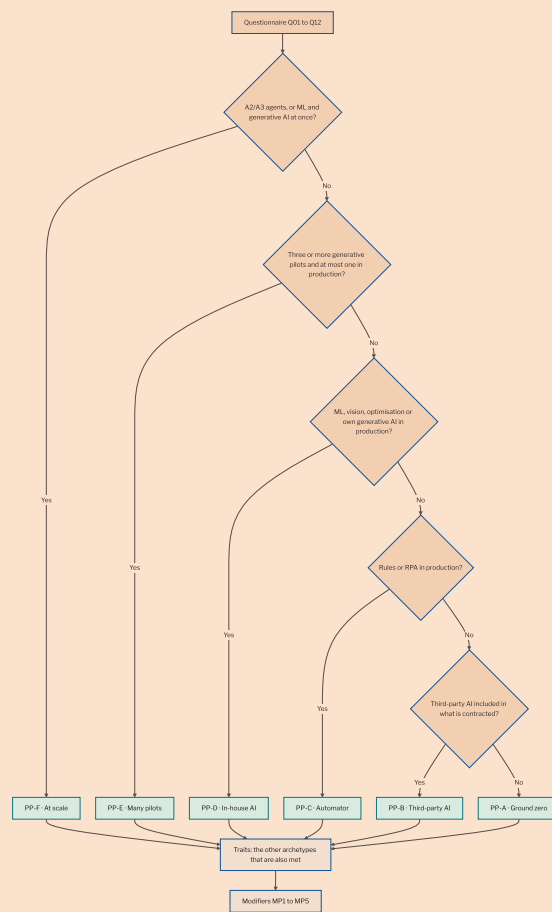

Source: SEVEN-G

Example: a company with ML in production, four generative pilots not in production and RPA receives **PP-E with traits PP-D and PP-C**. It starts by stopping or scaling the pilots, but it also regularises its models and makes use of its automation centre.

2.3 Modifiers

Code	Modifier	Effect on the journey
MP1	Regulated sector (financial services, insurance, healthcare, energy, public sector...)	Brings forward the inventory with classification (HI-05), regulatory mapping (34) and resilience (<u>DORA</u> or <u>NIS2</u> , where applicable).
MP2	Decisions about people, high risk or direct exposure to customers	Brings forward the impact assessments (P11, P47, P48), human oversight (P17) and the independent risk owner (HI-10).
MP3	Company-level Enterprise scope (90 §2.2)	Enterprise timetable of 90 §6.2. Without MP3, Lite timetable and minimum path of 90 §2.4.
MP4	Reusable prior governance (model validation, data committee, centre of excellence, certified management system)	The corresponding milestones are mapped and validated : what exists is adapted and the correspondence is documented, instead of creating it anew (section 4.3, rule 3).
MP5	No sponsor in senior management	Blocks : before any other milestone, the prerequisites of 90 §3 must be met. It is not one more milestone: it is a precondition.

Why it matters. Two companies of the same archetype do not have the same journey if one is supervised by a sector regulator or makes decisions about people. The modifiers capture those differences without multiplying the archetypes.

2.4 Classification questionnaire

Twelve questions. The answers refer to what is **in production** (in real use), unless the question says otherwise. Tool T23 proposes them from the T01 register when there is one.

Code	Question	Answers	Feeds
Q01	What types of systems are in production today? (several answers; if there is generative AI, how many cases: one or more than one)	None · rules or RPA · third-party AI included in products or assistants · predictive ML, vision or optimisation · generative AI integrated into processes · agents that execute actions (A2/A3)	Archetypes; technology footprint (11 §7.6)

Code	Question	Answers	Feeds
Q02	How many AI pilots or proofs of concept are under way?	0 · 1–2 · 3–5 · more than 5	PP-E
Q03	How many of those pilots are generative AI?	None · some · most	PP-E
Q04	Is there evidence of unauthorised use of AI assistants with company data?	Yes · No · Not known	Priority of HI-02 and HI-03
Q05	What governance exists today over models, automation or data?	None · partial (model validation, centre of excellence, data committee) · formal system	MP4
Q06	Is there an inventory of AI systems?	No · partial · complete with an owner	Priority of HI-05
Q07	Is the company in a regulated sector?	Yes · No	MP1
Q08	Does AI make or support decisions about people, is it exposed to customers or could it be high risk?	Yes · No · Not known	MP2
Q09	Is any Enterprise scope criterion of 90 §2.2 met?	Yes · No	MP3
Q10	Is there a member of senior management with written responsibility for AI?	Yes · No	MP5 (if no); D1.01
Q11	Do management or the board receive a periodic report or dashboard on AI?	None · management · the board	HI-15; D7.04 and D7.06
Q12	Does the company have its own data or AI development team?	Yes · No · through third parties	PP-B and PP-D; HI-20


"Not known" is treated as "yes" for priority purposes: if nobody knows whether there is unauthorised use or decisions about people, finding out comes first.

The five stages

Stage	Objective	Reference in document 90
E1 · Start	There is a sponsor and a mandate, and it is known what AI exists.	Week 1 and month 1 (90 §4.2)
E2 · Organise	Everything is in the register and in the inventory, and decisions are taken on the portfolio.	Months 1–3 (90 §4.2–§4.3)
E3 · Govern	Bodies, segregated roles, risks and lifecycle in operation.	Months 3–6 (90 §4.4, §6.1)
E4 · Measure	Value measured, dashboard at management and board level, operation under control.	Months 4–12 (90 §6.1)
E5 · Scale and review	Audit, annual C5 review, recalculated index and declaration of application.	Months 12–18 (90 §6.1–§6.2)

The five stages of the journey

Each stage groups milestones; the starting point changes the order within them, not the stages



Source: SEVEN-G

The stages overlap: a company may be measuring the value of its first cases (E4) while it finishes regularising the older ones (E3). What is not done is to skip a stage.

The journey milestones

4.1 What each milestone is, who does it and how it is substantiated

Each milestone states what must be in place, who leads it, with which template or tool, **which question from document 11 substantiates it** and the base month from document 90 (Lite /

Enterprise).

Milestone	Stage	What must be in place	Who	Evidence	Question 11	Base month (Lite / Enterprise)
HI-01	E1	Sponsor in senior management and implementation mandate with a perimeter	Board or chief executive; sponsor	P32	D1.01	Week 1
HI-02	E1	Inventory of corporate use and of unauthorised use of AI	AI Office; security	P05; T01 (T02); T21	D6.03	1 / 1
HI-03	E1	Acceptable use policy and basic literacy	AI Office; people function	31; P43; P45	D1.04; D5.03	3 / 3
HI-04	E2	Use case record and initiative register with every idea and pilot in its real phase	AI Office; product owners	P01; T01	D2.01; D2.03	1-3 / 1-3
HI-05	E2	Complete inventory with regulatory classification, intensity and owner, including third-party AI	AI Office; risk; legal	P04; P05; P07; 32; 36 §8	D6.05	6 / 9
HI-06	E2	C1 diagnosis: verified maturity, transformation index and technology footprint	AI Office; independent assessor	P33; P34; T15; T14	D7.08	1-2 / 1-2
HI-07	E2	Thesis, ambition by sphere and risk appetite approved by the board (C2)	Sponsor; board	P35; 13	D1.05	3 / 3-4
HI-08	E3	AI Committee, AI Office and board committee set up	Executive committee; board	P38; 30	D1.07	3 / 4
HI-09	E3	Segregated roles in each initiative: product, technical and operations owners, independent risk owner and AI Auditor (in Enterprise, at every <i>gate</i>)	AI Committee	P03; P41; 01 §8	D1.08	3 / 4
HI-10	E3	Independent AI Risk Owner and risk register with the scale of document 33 from phase 3	AI Committee; risk	33; P12; P13; T06	D6.04; D6.06	6 / 9

Milestone	Stage	What must be in place	Who	Evidence	Question 11	Base month (Lite / Enterprise)
HI-11	E3	Lifecycle with recorded <i>gates</i> for every new initiative	AI Office; <i>gate</i> decision-makers	20; 21; 22; P29; T03	D2.06	4 / 6
HI-12	E3	Regularisation of what is in production (review equivalent to G7, highest risk first)	Operations owners; AI Auditor	90 §5; 14 §11; P30	D4.07	6–12 / 6–12
HI-13	E2	Decision to stop or scale each pilot, with G3 as the stop gate and the T01 funnel	AI Committee	21 §6.4; T01	D2.04; D2.09	4 / 6
HI-14	E4	Value measurement rules, baseline and falsifiable hypothesis in each initiative from G2	Management control; business owners of the benefit	40; P08; P09; T11	D2.08; D7.03; D7.05	6 / 9
HI-15	E4	Periodic report to management and board dashboard	AI Office; board committee	60; P67; T17	D7.04; D7.06; D1.09	3 (management) · 6 / 9–12 (board)
HI-16	E3	Agent security and requirements on suppliers N1–N3	Security; procurement; risk	35; 36; P14; P18; P55	D6.08	Before G5
HI-17	E4	Operation under control: manual, monitoring and drift, tested rollback and a current R6	Operations owners	52; P24; P25; P65	D4.05; D4.06; D4.07	9 / 12–15
HI-18	E4	Nonconformities and incidents with the process of 01 §12	Risk; internal audit	37; P50; P26	D6.07	6 / 9
HI-19	E4	Adoption and people: adoption plan, released capacity kept separate from savings and information to workers' representatives	People function; business owners of the benefit	23; 50; P20; T20	D5.07; D5.08; D5.09	Before G4
HI-20	E3	Data and knowledge with an owner, legal basis and validity, including generative AI sources	Data owners; data protection	51; P64	D3.03; D3.05; D3.08	6 / 9
HI-21	E5	First audit of the framework by the third line or by an external party	Internal audit	38; P58–P61	D6.10	12 / 12

Milestone	Stage	What must be in place	Who	Evidence	Question 11	Base month (Lite / Enterprise)
HI-22	E5	C5 review: maturity recalculated with the same questionnaire, index, revised thesis and declaration of application	AI Committee; board	P37; P61; 01 §14	D1.11	6–12 / 13–18

4.2 Priority of each milestone according to the starting point

Keys: **1**, start now (months 1–2); **2**, in its stage (months 3–6); **3**, later (months 7–18); **C**, map and validate what already exists; **D**, when the trigger appears (first initiative in that phase, first agent, first supplier...); **·**, does not apply yet.

Milestone	PP-A	PP-B	PP-C	PP-D	PP-E	PP-F
HI-01	1	1	1	1	1	1
HI-02	1	1	1	1	1	1
HI-03	1	1	2	2	1	1
HI-04	1	2	1	1	1	1
HI-05	2	1	2	1	2	1
HI-06	1	1	1	1	1	1
HI-07	2	2	2	2	2	2
HI-08	2	2	C	C	2	1
HI-09	2	2	2	1	2	1
HI-10	D	2	2	1	1	1
HI-11	2	2	2	2	1	1
HI-12	·	2	2	1	2	1
HI-13	D	D	2	2	1	2
HI-14	2	2	2	2	1	2
HI-15	2	2	2	2	2	1

Milestone	PP-A	PP-B	PP-C	PP-D	PP-E	PP-F
HI-16	D	1	D	2	2	1
HI-17	D	.	D	1	D	1
HI-18	3	2	2	2	2	1
HI-19	D	1	2	2	2	1
HI-20	D	2	2	C	2	1
HI-21	3	3	3	3	3	3
HI-22	3	3	3	3	3	3

The base month in document 90 is the limit; the priority only brings it forward or pushes it back within that limit. The modifiers adjust the priority as follows:

- **Q04** at "yes" or "don't know" moves HI-02 and HI-03 to **1**.
- **MP1** and **MP2** move HI-05 and HI-10 to **1** (and, with MP2, HI-19 when there is an initiative that changes people's work).
- **MP4** changes to **C** the milestones covered by existing governance, provided that the correspondence is documented.
- **MP5** blocks the whole journey until HI-01 is met.

4.3 Journey rules

1. **HI-01 comes before everything.** With MP5, the journey does not start.
2. **No required milestone disappears.** "." only means "does not apply yet": the milestone appears when its trigger is activated (01 §9; triggers in document 94).
3. **Mapping and validating requires verified correspondence.** "C" means adapting what already exists and documenting its correspondence with what SEVEN-G requires, verified by whoever verifies the *gates* (D31). A declared "we already have it" does not count.
4. **A milestone is met when its question from document 11 is at "Yes" in a verified assessment.** Until then it may be "in progress". In this way, advancing along the journey **is** raising maturity with evidence, not completing a parallel checklist.
5. **Traits.** With traits, each milestone takes the most urgent priority between the main archetype and its traits, in this order: 1, 2, C, D, 3, .
6. **The destination is the same.** The declaration of application (01 §14) requires the same of every archetype, within the time limits of 90 §6.2.

Why it matters. The journey answers "what do I do on Monday" without lowering what is required. Because each milestone is substantiated with a question from document 11, the committee can follow progress with the same diagnosis the board will use.

05

What falls to each role

The table is derived from the "Who" column of section 4.1: it adds no responsibilities.

Role	E1 · Start	E2 · Organise	E3 · Govern	E4 · Measure	E5 · Scale and review
Board	HI-01	HI-07	HI-08	HI-15 (dashboard)	HI-22
Sponsor	HI-01	HI-07	—	—	—
Executive committee	—	—	HI-08	—	—
AI Committee	—	HI-13	HI-09, HI-10	—	HI-22
AI Office	HI-02, HI-03	HI-04, HI-05, HI-06	HI-11	HI-15	—
AI Risk Owner	—	HI-05	HI-10, HI-16	HI-18	—
AI Auditor	—	—	HI-12	—	—
Internal audit	—	—	—	HI-18	HI-21
Security and procurement	HI-02	—	HI-16	—	—
Legal and data protection	—	HI-05	HI-20	—	—
Product owners	—	HI-04	—	—	—
Operations owners	—	—	HI-12	HI-17	—
Management control	—	—	—	HI-14	—

Role	E1 · Start	E2 · Organise	E3 · Govern	E4 · Measure	E5 · Scale and review
Business owners of the benefit	—	—	—	HI-14, HI-19	—
People function	HI-03	—	—	HI-19	—
Data owners	—	—	HI-20	—	—
Independent assessor	—	HI-06	—	—	—

In a small organisation several of these functions are performed by the same person, within the limits of 90 §7 and 30 §11: whoever builds does not verify or decide on their own work, and risk clearance is issued by someone independent of the team.

06

Three example journeys

The three cases are **fictitious** and only illustrate how the order changes.

6.1 Medium-sized industrial company, PP-A

An industrial company of about a thousand employees has no AI in production. The questionnaire reveals unauthorised use of generative assistants in engineering and procurement (Q04 = yes) and that nobody in senior management has been assigned AI in writing (Q10 = no: **MP5**).

- **Week 1.** The chief executive assigns AI to the chief operating officer and signs the mandate (HI-01). Only then does the journey begin.
- **Months 1–2.** Inventory of unauthorised use (HI-02), acceptable use policy and a literacy session for engineering and procurement (HI-03), T01 register with the seven ideas in circulation (HI-04) and C1 diagnosis (HI-06).
- **Months 3–6.** Thesis and appetite approved by the board (HI-07), committee and a one-person part-time AI Office (HI-08) and lifecycle for the two ideas that pass G0 (HI-11). The risk register (HI-10) arrives when the first initiative enters phase 3.

6.2 Insurer, PP-D with trait PP-E, MP1, MP2 and MP4

An insurer has twelve predictive models in production (pricing, fraud, churn), a model validation function and five generative AI pilots not in production. It is a regulated sector (**MP1**), it makes decisions about people (**MP2**) and it has prior governance (**MP4**).

- **Months 1–2.** Mandate (HI-01) and complete inventory with regulatory classification, in which pricing is identified as potentially high risk (HI-05, brought forward by MP1). Segregated roles in the twelve models (HI-09). Risk register with the scale of document 33 (HI-10). The existing model committee **is mapped and validated** as part of the AI Committee, with its correspondence documented (HI-08 at C).
- **Months 2–4.** The five pilots go through G3 (HI-13): two proceed, three are stopped with their reason recorded. Regularisation of the models starts with pricing (HI-12).
- **Months 4–9.** Drift and monitoring under document 52 in production (HI-17), knowledge sources for the two generative cases that proceed (HI-20) and board dashboard (HI-15).

6.3 Services company, PP-B

A professional services company has deployed a generative assistant in the office suite for 1,800 people and uses three SaaS products with AI included. It does not develop.

- **Months 1–2.** Inventory of the AI included in what is contracted (HI-05, with 36 \$8), N1–N3 requirements on the three suppliers and on the assistant's supplier (HI-16), acceptable use policy (HI-03) and adoption plan (HI-19).
- **Months 2–6.** The assistant is registered as **a single cross-unit initiative** and measured by unit with the ladder of 40 \$7.2: full cost, adoption, declared released capacity and materialised value. Two units below the adoption threshold review the deployment.
- **Later.** When the first in-house case appears, the technical cycle and operation are activated (HI-17, at D).

07

Relationship with other documents

Document	Relationship
90 · Implementation guide	Defines what must be in place and within what maximum time limit. This document orders those elements according to the starting point.
11 · Maturity model	Each milestone is substantiated with a question from the questionnaire. The three-lens reading (§7.6) adds the technology footprint, which is obtained from the same answers to Q01 or from the T01 register, and the minimum governance it requires.
12 · Transformation index	The impact reach (§3.7) says whether AI touches tasks, processes, people or the business model.
94 · Obligation matrix	Level of each document, template and tool, and triggers that activate the milestones marked "D".

Document	Relationship
01 · Foundational methodology	Conditions of the declaration of application (§14), the same for every archetype.

08

Associated tools and templates

Code	Tool or template	Use in the journey
T23	Implementation journey	Questionnaire, archetype, traits and modifiers; journey prioritised by stage and by role; milestones met according to T15; printable plan and CSV.
T01	Initiative register	Proposes the answers to Q01 to Q03 from the initiatives in use and the pilots.
T15	Maturity diagnosis	Marks milestones as met when their questions are at "Yes"; three-lens view.
P32	Implementation mandate	HI-01.
P33 · P34	C1 report · maturity questionnaire and report	HI-06.
P35	Thesis and appetite	HI-07.

09

Related documents

Document	Relationship
90 · Implementation guide	Scope, prerequisites, 90-day plan, regularisation and roadmap.
11 · Maturity model	Questions that substantiate each milestone and three-lens reading.
12 · Transformation index	Impact reach.
14 · Portfolio management	Regularisation of initiatives that predate the framework (§11).
30 · Governance model	Bodies, roles and incompatibilities; adaptation to small organisations (§11).

Document	Relationship
54 · Organising the company for AI	Where use cases come from and what comes in without passing through the gate.
94 · Obligation matrix	Obligation levels and triggers.

10

Version control

Version	Date	Changes
0.1	28-09-2026	First version: six starting points, assignment rule, five modifiers, twelve-question questionnaire, five stages, twenty-two milestones with their evidence, the question from document 11 that substantiates them and their priority by archetype, roles by stage and three fictitious journeys. Assignment thresholds and priorities, to be validated.
0.2	28-09-2026	Thresholds and priorities validated. The assignment rule no longer leaves in PP-A a company with in-house AI in production: PP-F becomes "A2 or A3 agents, or ML and generative AI at once" and PP-D, renamed "In-house AI in production", includes generative AI integrated into processes. HI-16 (suppliers) rises to 2 in PP-E, because generative pilots use third-party models with company data, and HI-20 (data and knowledge) goes from · to 2 in PP-B, because corporate assistants access the company's knowledge sources.

External sources cited

Links to the official or primary source, checked before publication. Always verify the version in force on the date of use.

Directive (EU) 2022/2555 of the European Parliament and of the Council of 14 December 2022 on measures for a high common level of cybersecurity across the Union (NIS 2 Directive) · <https://eur-lex.europa.eu/eli/dir/2022/2555/oj/eng> · Parlamento Europeo y Consejo de la UE · 14-12-2022

Regulation (EU) 2022/2554 of the European Parliament and of the Council of 14 December 2022 on digital operational resilience for the financial sector (DORA) · <https://eur-lex.europa.eu/eli/reg/2022/2554/oj/eng> · Parlamento Europeo y Consejo de la UE · 14-12-2022
